ID		Task Mode	Task Name	Duration	Start	Finish
1	✓		Initial Survey	66 days	Tue 8/1/17	Tue 10/31/17
2			NEPA	847 days	Sun 1/1/17	Sun 3/29/20
3			**50% Preliminary Design**	**826 days**	**Sun 1/1/17**	**Mon 3/2/20**
4			Roadway	817 days	Sun 1/1/17	Sat 2/15/20
5	✓		Wetland Delineation	22 days	Sun 10/1/17	Mon 10/30/17
6	✓		Typical Sections	23 days	Sun 10/1/17	Tue 10/31/17
7	✓		Preliminary Bridge Concepts	22 days	Fri 9/1/17	Sat 9/30/17
8	✓		Plan and Profile Sheets	109 days	Fri 9/1/17	Wed 1/31/18
9	✓		Title Sheet	7 days	Tue 5/1/18	Wed 5/9/18
10			Estimate of Quantities	14 days	Mon 7/1/19	Thu 7/18/19
11			Preliminary Probable Opinion of Cost	14 days	Mon 7/1/19	Thu 7/18/19
12			Preliminary QC/QA	14 days	Sat 2/1/20	Wed 2/19/20
13			Preliminary Plans	8 days	Thu 2/20/20	Mon 3/2/20
14			**100% Design**	**120 days**	**Wed 1/1/20**	**Tue 6/16/20**
15			General Notes	22 days	Wed 1/1/20	Thu 1/30/20
16			Gaurdrail Details	22 days	Wed 1/1/20	Thu 1/30/20
17			Grading and Wetland Impacts	22 days	Wed 1/1/20	Thu 1/30/20
18			Superelevation Table	22 days	Wed 1/1/20	Thu 1/30/20
19			Signage and Pavement Marking	22 days	Wed 1/1/20	Thu 1/30/20
20			Plan Revisions	20 days	Sat 2/1/20	Thu 2/27/20
21			Bridge Design	42 days	Sun 3/1/20	Mon 4/27/20
22			QC/QA	14 days	Fri 5/1/20	Wed 5/20/20
23			Fianl Plans and Specifications	20 days	Wed 5/20/20	Tue 6/16/20
24			**Bidding**	**14 days**	**Mon 8/3/20**	**Thu 8/20/20**
25			Advertisement for Bids	14 days	Mon 8/3/20	Thu 8/20/20
26			**Construction**	**283 days**	**Thu 10/1/20**	**Mon 11/1/21**
27			Preconstruction Meeting	1 day	Thu 10/1/20	Thu 10/1/20
28			Begin Construction when Weather Allows	1 day	Thu 10/15/20	Thu 10/15/20
29			Traffic Control Setup	7 days	Thu 10/15/20	Fri 10/23/20
30			Temporary Erosion Control	7 days	Thu 10/15/20	Fri 10/23/20
31			**Bridge**	**165 days**	**Sun 11/1/20**	**Fri 6/18/21**
32			Bridge Removal	7 days	Sun 11/1/20	Mon 11/9/20
33			Bridge Construction	132 days	Tue 12/1/20	Wed 6/2/21
34			Bridge Guardrail	14 days	Tue 6/1/21	Fri 6/18/21
35			**Paving**	**89 days**	**Tue 6/1/21**	**Fri 10/1/21**
36			Shoulder/Approaches	22 days	Tue 6/1/21	Wed 6/30/21
37			County Road 17 - CSHH1	46 days	Thu 7/1/21	Thu 9/2/21
38			Bridge Paving	23 days	Wed 9/1/21	Fri 10/1/21
39			Misc. (Signing/Pavement Marking/Rumble Strips)	22 days	Fri 10/1/21	Mon 11/1/21
40			Seeding	22 days	Fri 10/1/21	Mon 11/1/21
41			Incidentals	22 days	Fri 10/1/21	Mon 11/1/21
42			**Project Closeout**	**45 days**	**Mon 11/1/21**	**Fri 12/31/21**
43			Final Documentation	22 days	Mon 11/1/21	Tue 11/30/21
44			Closeout Review	23 days	Wed 12/1/21	Fri 12/31/21
45			Final Completion	1 day	Fri 12/31/21	Fri 12/31/21
46						

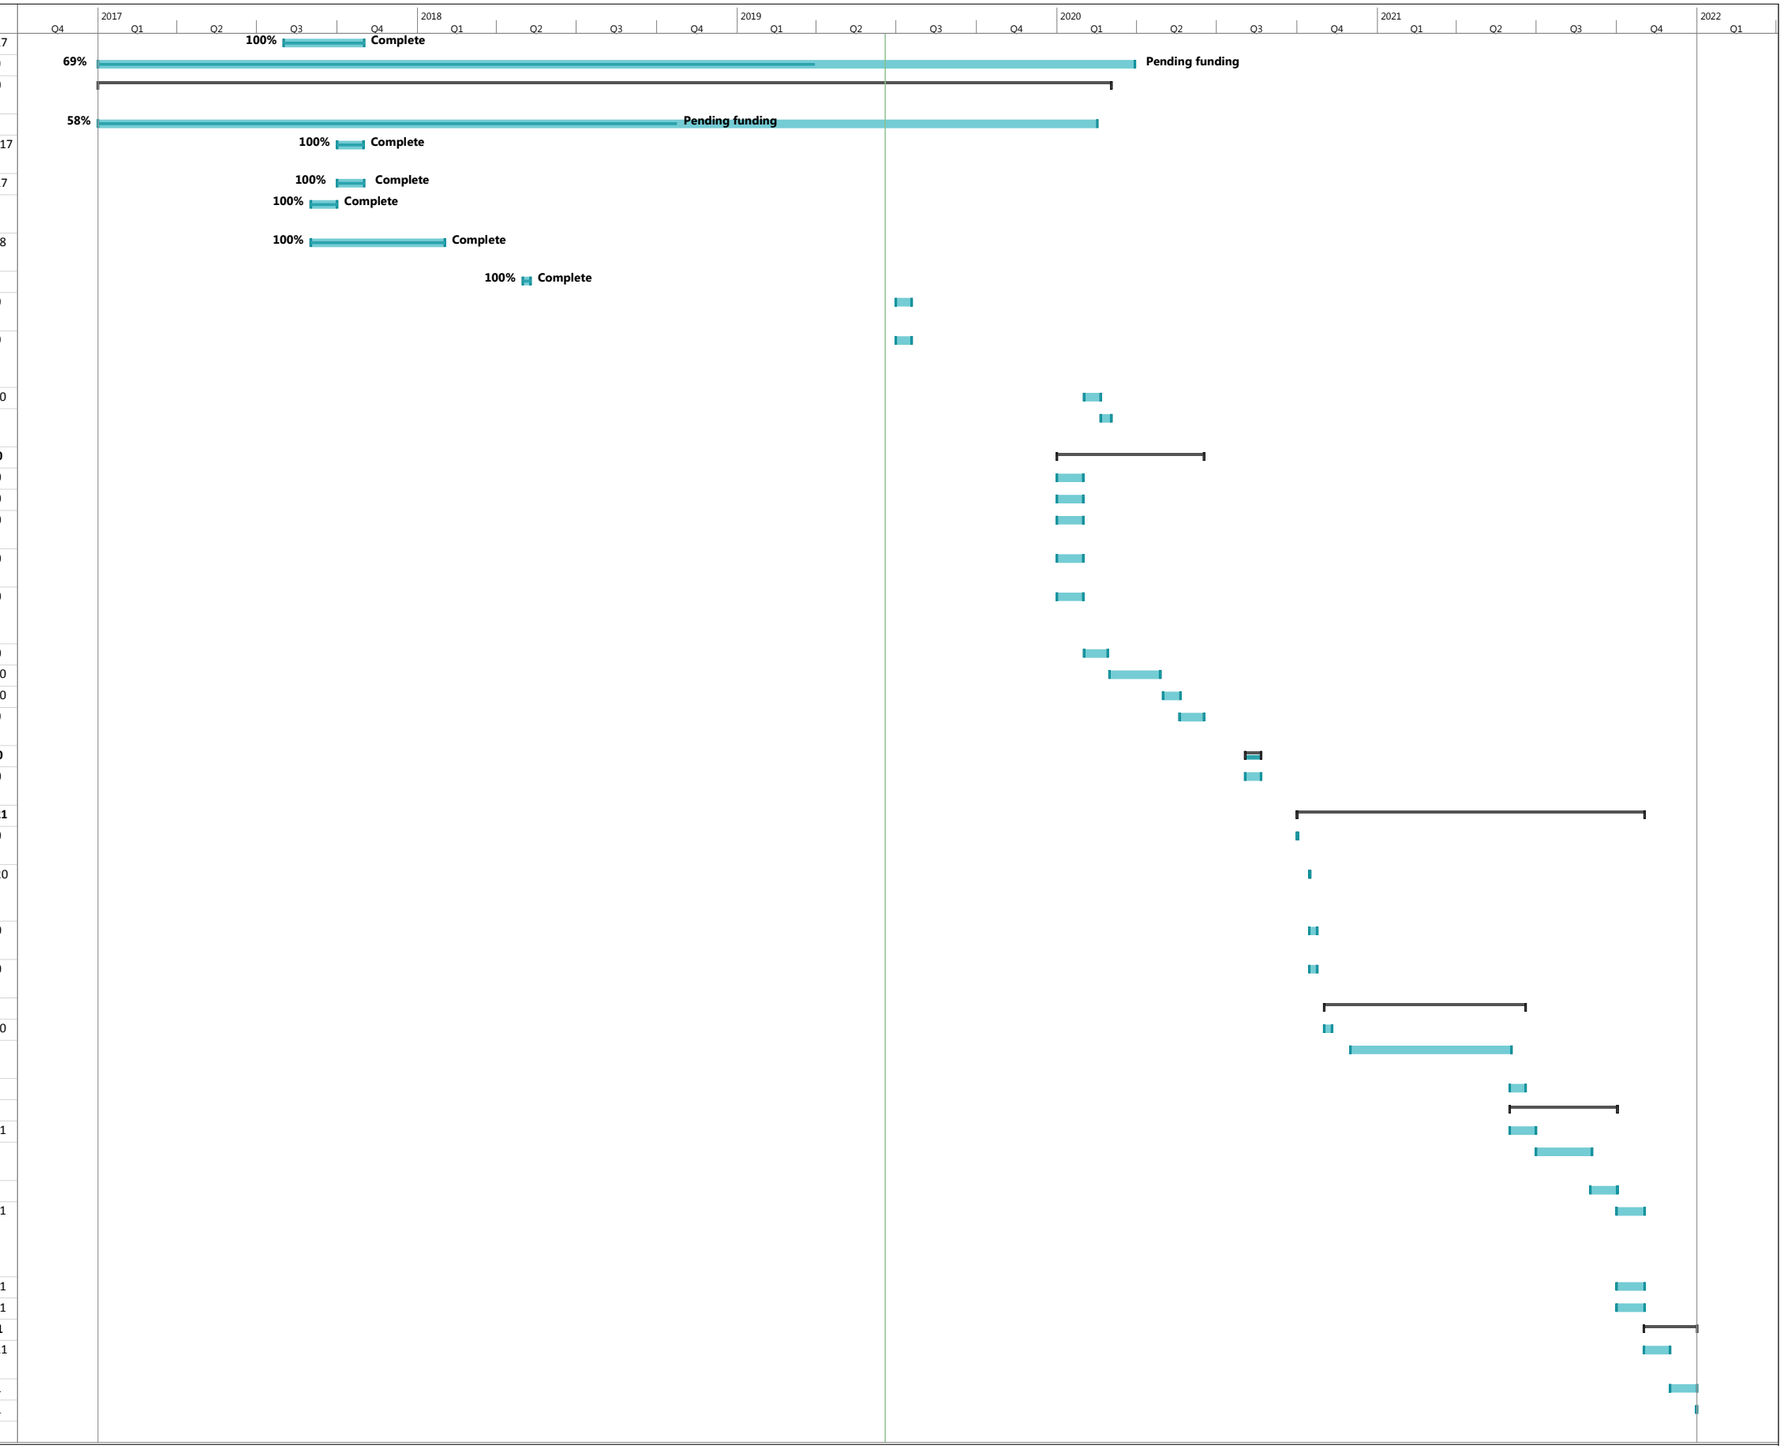

Project: Multi-State Regional Co
Date: Wed 6/19/19

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
